

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Feb 4, '18							Feb 11, '18				
							S	M	T	W	T	F	S	S	M	T	W	T
1																		
2		Mobilize on Site	30 days	Mon 2/19/18	Fri 3/30/18													
3		Phase 1 - Locations 1, 2, & 3	5 days	Mon 2/19/18	Fri 2/23/18													
4		SWPP / BMP	1 day	Mon 2/19/18	Mon 2/19/18													
5		Sawcut locations	1 day	Mon 2/19/18	Mon 2/19/18													
6		Demo concrete / grade /compact sub base	2 days	Mon 2/19/18	Tue 2/20/18													
7		Inspection	1 day	Tue 2/20/18	Tue 2/20/18													
8		Pour concrete sidewalk	2 days	Wed 2/21/18	Thu 2/22/18													
9		Install mosaic murals	2 days	Thu 2/22/18	Fri 2/23/18													
10		Phase 2 - Locations 4, 5. & 6	5 days	Mon 2/26/18	Fri 3/2/18													
11		SWPP / BMP	1 day	Mon 2/26/18	Mon 2/26/18													
12		Sawcut locations	1 day	Mon 2/26/18	Mon 2/26/18													
13		Demo concrete / grade /compact sub base	2 days	Mon 2/26/18	Tue 2/27/18													

Project: Revised Schedule to Inc Date: Mon 2/5/18

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Feb 4, '18							Feb 11, '18						
							S	M	T	W	T	F	S	S	M	T	W	T		
14		Inspection	1 day	Tue 2/27/18	Tue 2/27/18															
15		Pour concrete sidewalk	2 days	Wed 2/28/18	Thu 3/1/18															
16		Install mosaic murals	2 days	Thu 3/1/18	Fri 3/2/18															
17		Phase 3 Locations 7,8,& 9	5 days	Mon 3/5/18	Fri 3/9/18															
18		SWPP / BMP	1 day	Mon 3/5/18	Mon 3/5/18															
19		Sawcut locations	1 day	Mon 3/5/18	Mon 3/5/18															
20		Demo concrete / grade /compact sub base	2 days	Mon 3/5/18	Tue 3/6/18															
21		Inspection	1 day	Tue 3/6/18	Tue 3/6/18															
22		Pour concrete sidewalk	2 days	Wed 3/7/18	Thu 3/8/18															
23		Install mosaic murals	2 days	Thu 3/8/18	Fri 3/9/18															
24		Phase 4 -Locations 10, 11 & 15	5 days	Mon 3/12/18	Fri 3/16/18															
25		SWPP / BMP	1 day	Mon 3/12/18	Mon 3/12/18															
26		Sawcut locations	1 day	Mon 3/12/18	Mon 3/12/18															


Project: Revised Schedule to Inc Date: Mon 2/5/18

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Feb 4, '18							Feb 11, '18					
							S	M	T	W	T	F	S	S	M	T	W	T	
27		Demo concrete / grade /compact sub base	2 days	Mon 3/12/18	Tue 3/13/18														
28		Inspection	1 day	Tue 3/13/18	Tue 3/13/18														
29		Pour concrete sidewalk	2 days	Wed 3/14/18	Thu 3/15/18														
30		Install mosaic murals	2 days	Thu 3/15/18	Fri 3/16/18														
31		Phase 5 -Locations 13, 14 & 15	5 days	Mon 3/19/18	Fri 3/23/18														
32		SWPP / BMP	1 day	Mon 3/19/18	Mon 3/19/18														
33		Sawcut locations	1 day	Mon 3/19/18	Mon 3/19/18														
34		Demo concrete / grade /compact sub base	2 days	Mon 3/19/18	Tue 3/20/18														
35		Inspection	1 day	Tue 3/20/18	Tue 3/20/18														
36		Pour concrete sidewalk	2 days	Wed 3/21/18	Thu 3/22/18														
37		Install mosaic murals	2 days	Thu 3/22/18	Fri 3/23/18														
38		Phase 6 -Substantial Completion	5 days	Mon 3/26/18	Fri 3/30/18														
39		Substantial Completion	5 days	Mon 3/26/18	Fri 3/30/18														

Project: Revised Schedule to Inc Date: Mon 2/5/18


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

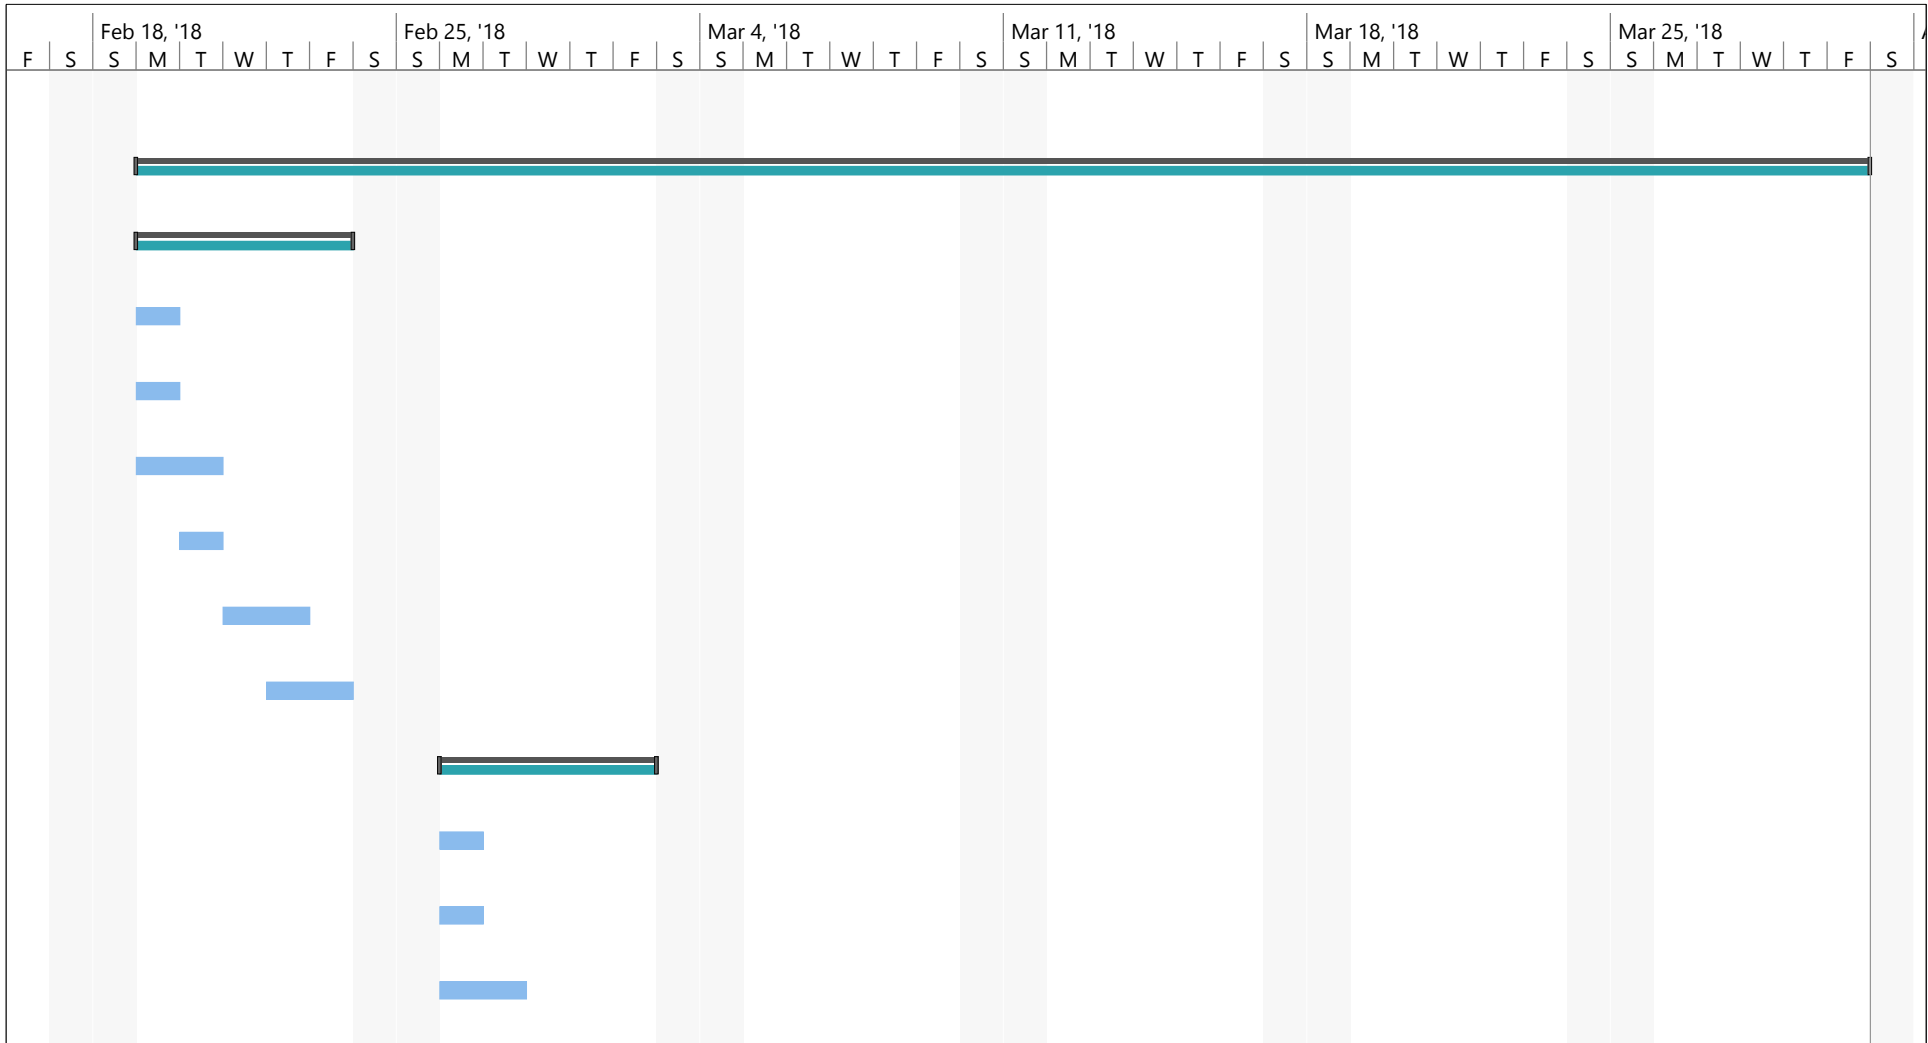

Project: Revised Schedule to Inc Date: Mon 2/5/18	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

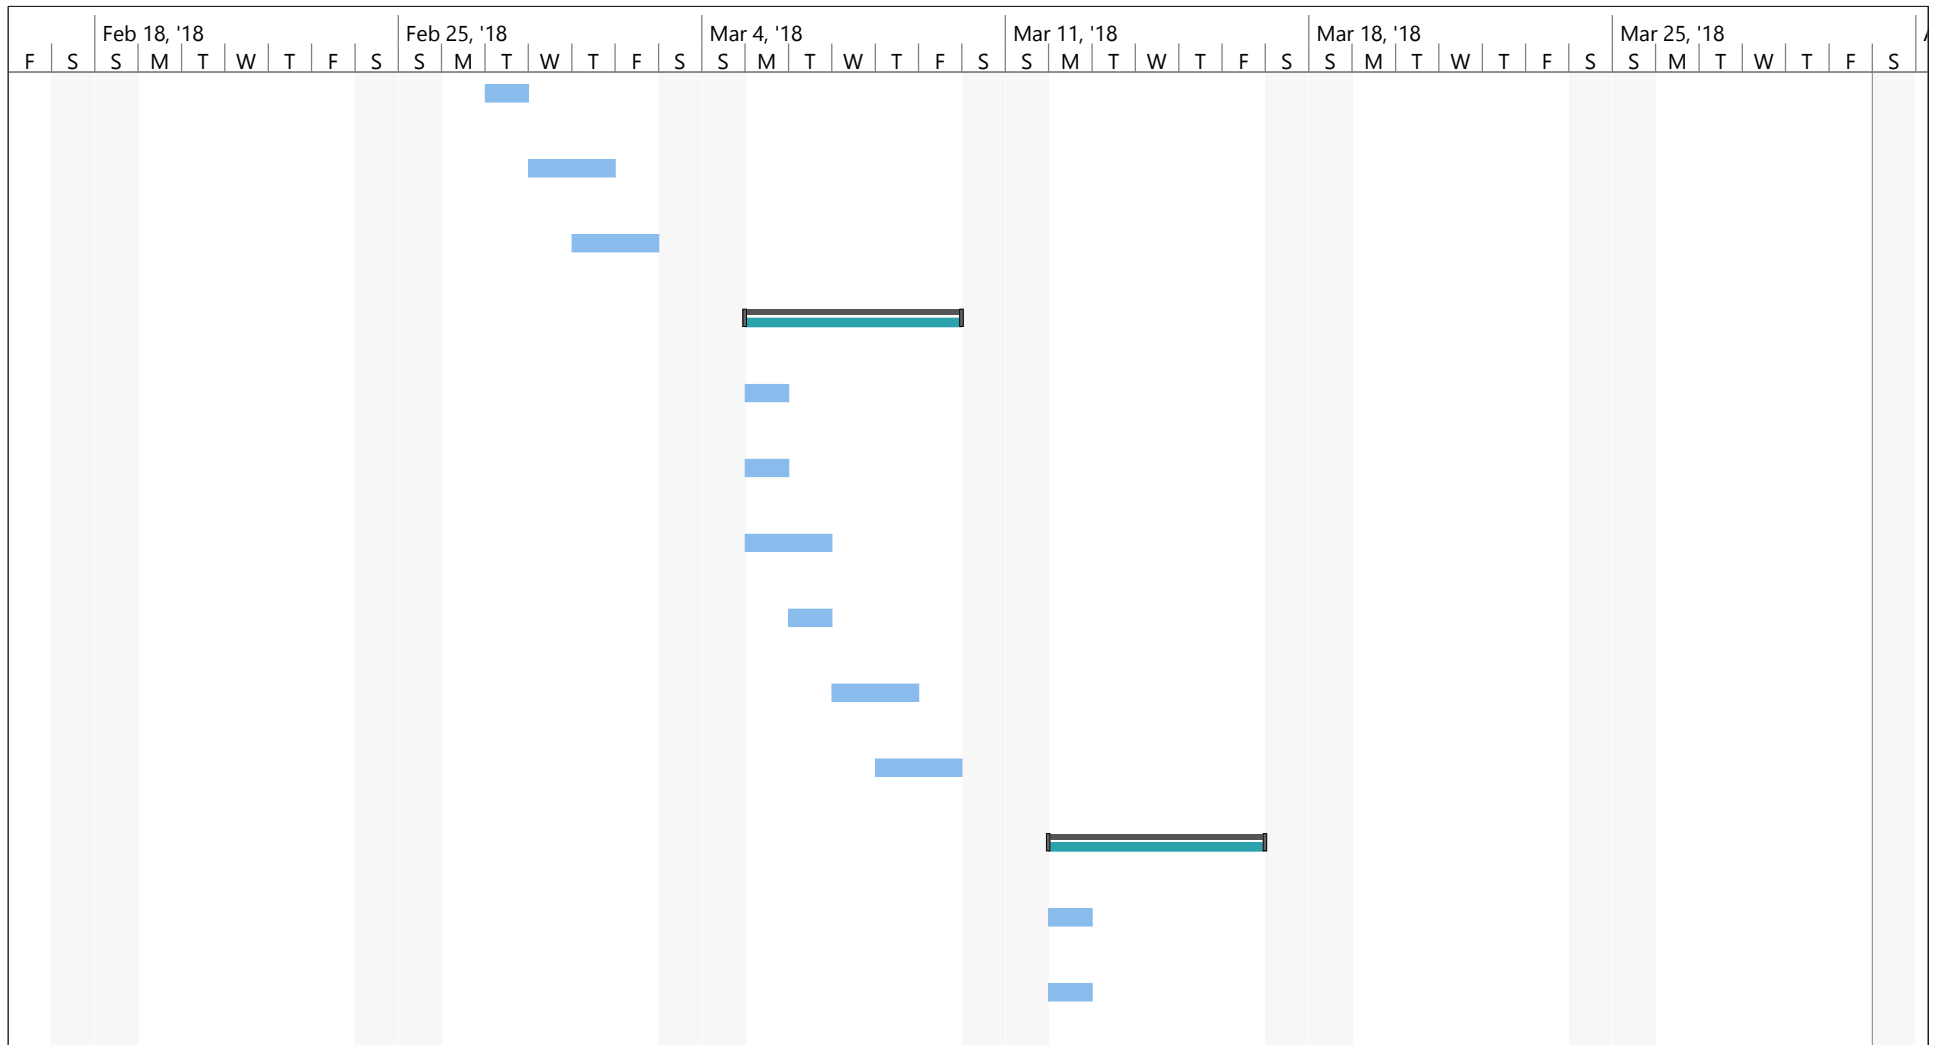

Project: Revised Schedule to Inc Date: Mon 2/5/18	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

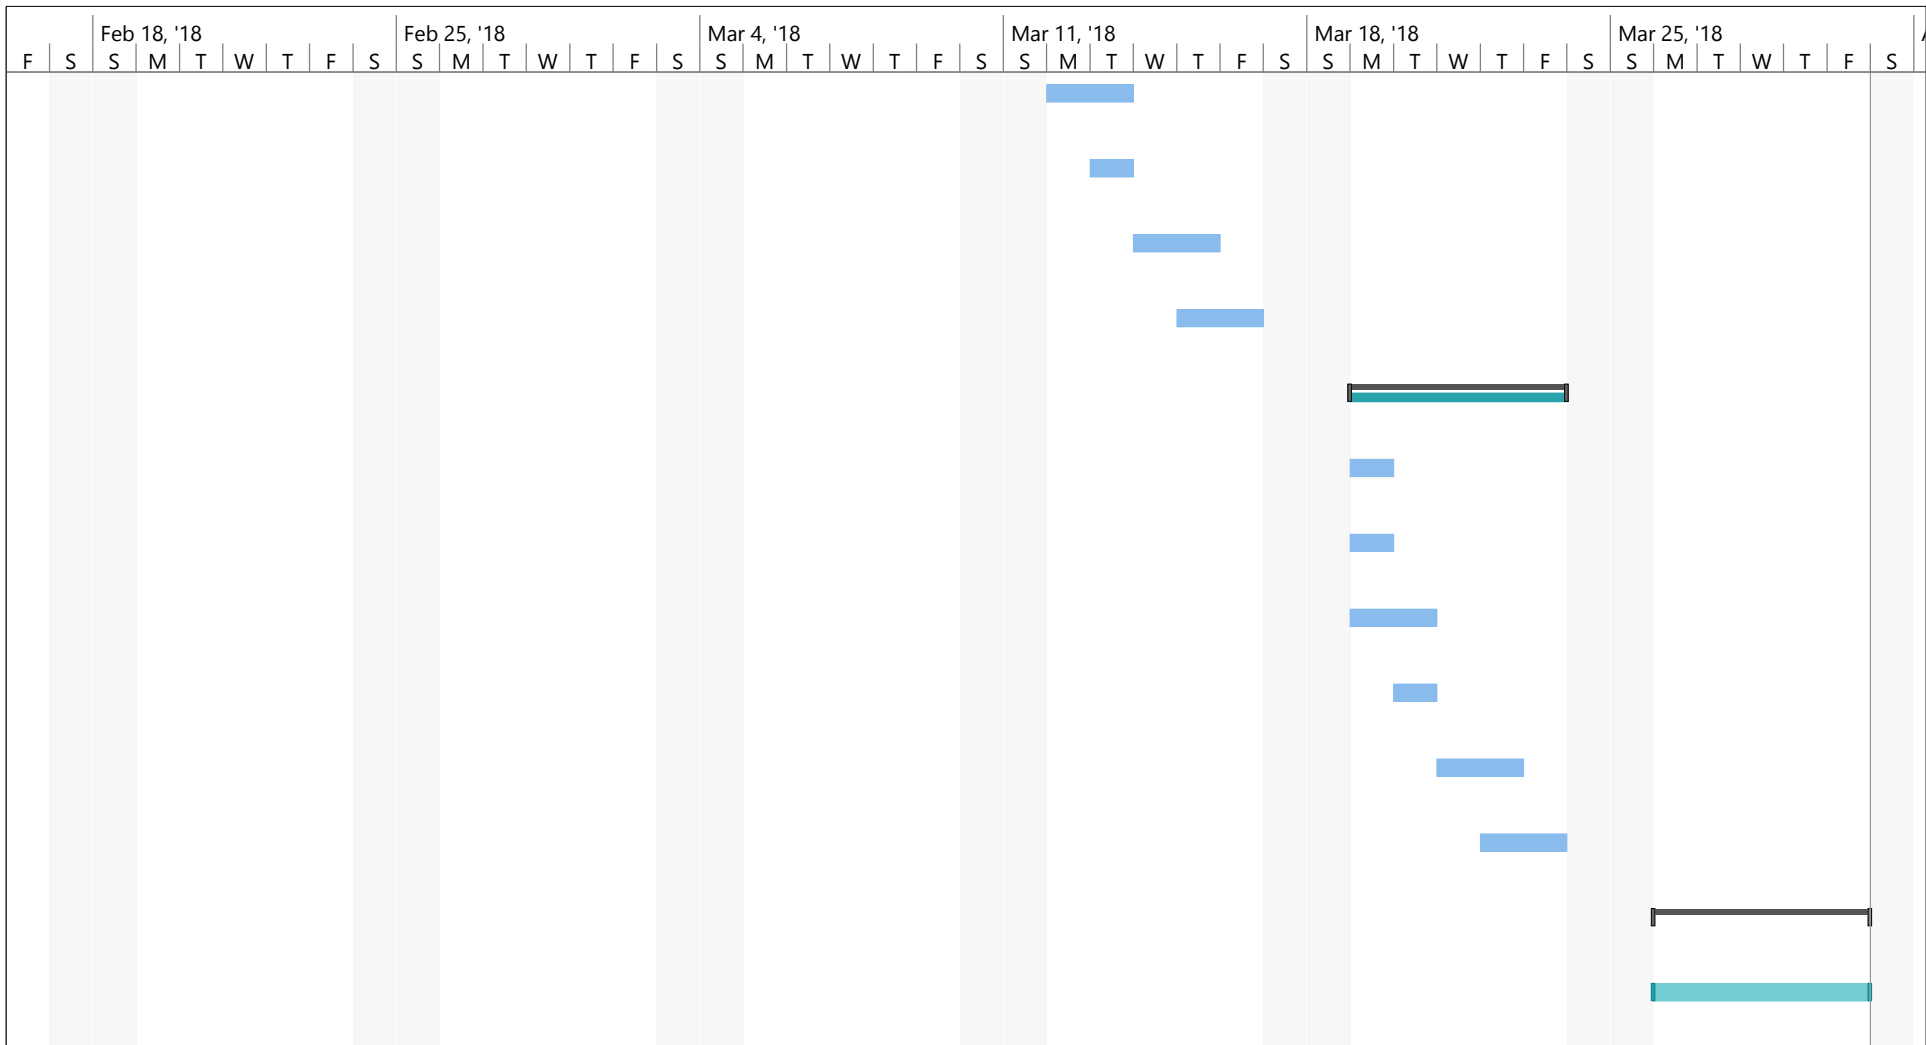

Project: Revised Schedule to Inc Date: Mon 2/5/18	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			
